

APPENDIX C
DAILY PHOTO LOGS

REMOVAL ACTION REPORT

**ROBERTO CLEMENTE TOWN PARK
400 BROADWAY
BRENTWOOD, NY 11717**

SEPTEMBER 21, 2015

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/1/2015

Photo 1



Description

Soccer field upon arrival of Enviroscience personnel on mobilization day

Photo 2



Description

Recharge basin upon arrival of Enviroscience personnel on mobilization day

Photo 3



Description

Trailer and container placing on mobilization day 1

Photo 4



Description




Photo 5



Description





Photo 6



Description



**Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779**

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/2/2015


Photo 1



Description

Gramercy water tank truck arrives on site.
CAT D25C

Photo 2

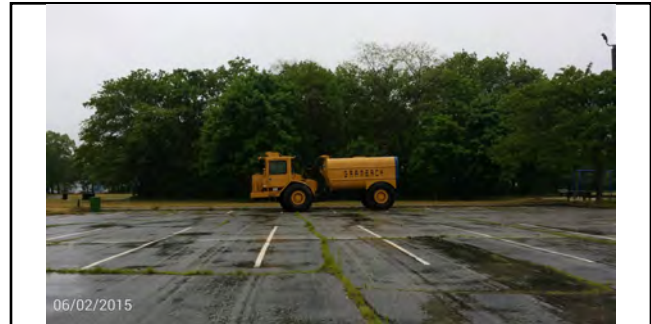

Description

Water tank truck placing on the Southwest
parking lot area.

Photo 3



Description

Container trailer arrives on site. CBL 9071

Photo 4



Description

Container trailer placing on the Southwest
parking lot area.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/3/2015

Photo 1



Description

CALLAHEAD portable toilets delivered at job site.

Photo 2



Description

A+ Technology Security personnel on site.

Photo 3



Description

Gramercy's wheel loader wa480 delivered at job site.

Photo 4



Description

Gramercy's wheel loader placing on the southwest parking lot area.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/4/2015

Photo 1



Description

Photo log tour Gramercy Group and
Enviroscience Consultants, Inc.

Photo 2



Description

CAT 303.5E Excavator delivered at job site.

Photo 3



Description

CAT 303.5E Excavator placing on the
southwest parking lot area.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/5/2015

Photo 1



Description

Gramercy's decontamination unit trailer delivered at job site.

Photo 2



Description

Decontamination unit placing by the northwest parking lot.

Photo 3



Description

Delineation of soccer field material.

Photo 4



Description

Delineation of soccer field material.

Photo 5



Description

Delineation of soccer field material.

Photo 6



Description

Delineation of soccer field material.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/8/2015

Photo 1



Description

Screen dust first shipment delivered at job site.

Photo 2



Description

Screen dust placing on the southwest parking lot.

Photo 3



Description

Office trailer delivered at job site.

Photo 4



Description

Office trailer set up on the east side of the park.

Photo 5



Description

Decontamination unit electrical set up.

Photo 6



Description

CAT 349F hydraulic excavator delivered at job site.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/8/2015

Photo 1



Description

S550 Bobcat and 450AJ Lift delivered at job site.

Photo 2



Description

Scale assembling at entrance to the park.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/9/2015

Photo 1



Description

Screen Dust second shipment delivered at job site.

Photo 2



Description

Dust-Buster units delivered at job site.

Photo 3



Description

Gramercy's Office Trailer delivered at job site.

Photo 4



Description

Open container delivered at job site.

Photo 5



Description

Disturbed material on southeast perimeter of soccer field.

Photo 6



Description

Disturbed material on north perimeter of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/10/2015

Photo 1



Description

Park pre-cleaning activities in progress.

Photo 2



Description

Park pre-cleaning activities in progress.

Photo 3



Description

Park pre-cleaning activities in progress.

Photo 4



Description

Upgrade on delineation of soccer field material.

Photo 5



Description

Upgrade on delineation of soccer field material.

Photo 6



Description

Upgrade on delineation of soccer field material.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/11/2015

Photo 1



Description

Park Sweeping activities in progress.

Photo 2



Description

Park Sweeping activities in progress.

Photo 3



Description

Tree trimming activities in progress.

Photo 4



Description

Tree trimming activities in progress.


Photo 5



Description

Water hose set up (south).

Photo 6

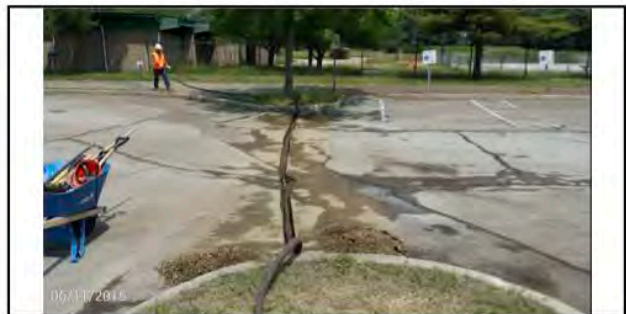

Description

Water hose set up (north).

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/11/2015

Photo 1



Description

Park's perimeter signage in place.

Photo 2



Description

Water hose set up on northwest parking lot.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/12/2015

Photo 1



Description

Rain drain filter set up.

Photo 2



Description

Truck lining station set up.

Photo 3



Description

Truck lining station set up.

Photo 4



Description

Scale calibration activities.

Photo 5



Description

Water hose set up on northwest parking lot.

Photo 6



Description

Water hose set up on northwest parking lot.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/15/2015

Photo 1



Description

Dust Screen third shipment delivered at job site.

Photo 2



Description

Weather station set up.

Photo 3



Description

Tire wash station located on the southwest parking lot.


Photo 4



Description

CAMP station set up.

Photo 5

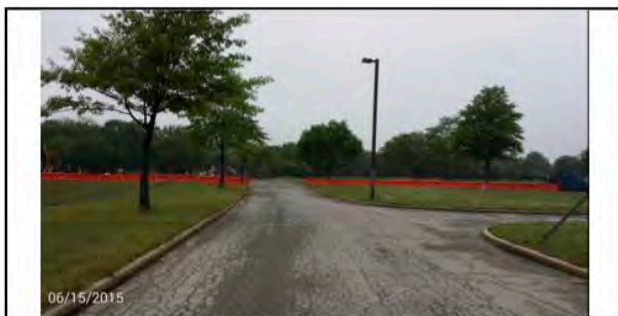

Description

Work area delineation.

Photo 6



Description

Work area delineation at recharge basin.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/16/2015

Photo 1



Description

Work area preparation activities by recharge basin.

Photo 2



Description

Work area preparation activities by recharge basin.

Photo 3



Description

Tire wash station water pump set up.

Photo 4



Description

Tire wash station water filtration system set up.

Photo 5



Description

Work area preparation activities north of soccer field.

Photo 6



Description

Work area preparation activities north of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/17/2015


Photo 1



Description

Dust screen fully assembled.

Photo 2

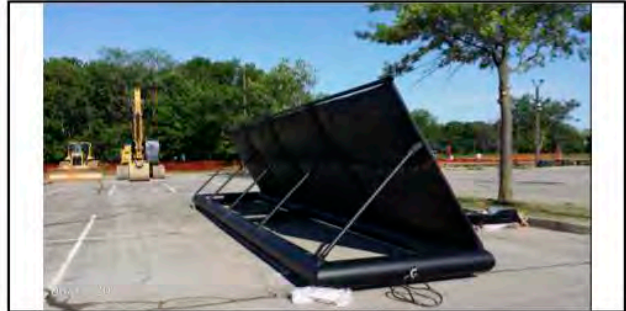

Description

Dust screen fully assembled.


Photo 3



Description

Work area preparation activities south of soccer field.


Photo 4

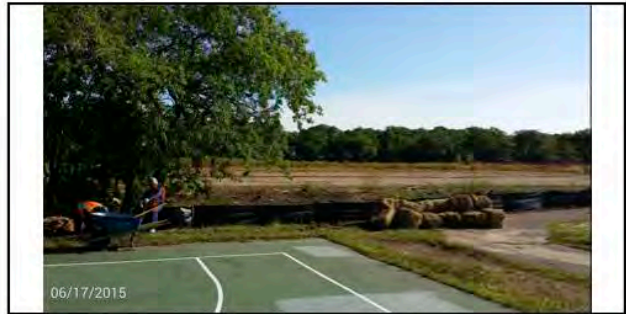

Description

Work area preparation activities south of soccer field.

Photo 5

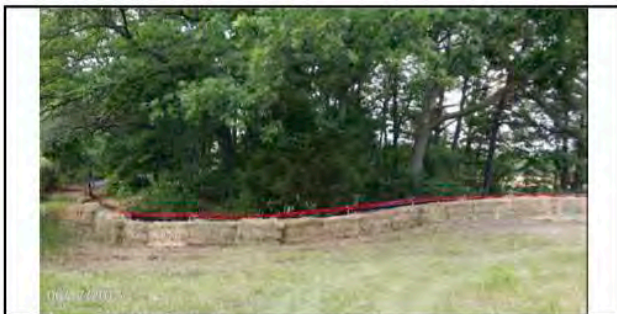

Description

Work area preparation activities west of soccer field.

Photo 6



Description

Work area preparation activities west of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/17/2015

Photo 1



Description

Water truck delivered at job site.

Photo 2



Description

Work area preparation activities south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/18/2015

Photo 1



Description

Work area fence signage.

Photo 2



Description

Work area fence signage.

Photo 3



Description

CAMP activities in progress.

Photo 4



Description

Truck road on soccer field work area.

Photo 5



Description

Truck road on soccer field work area.

Photo 6



Description

Work area preparation east of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/18/2015

Photo 1



Description

Dust buster test run.

Photo 2



Description

Dust buster test run.

Photo 3



Description

Waste container delivered at job site.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/19/2015

Photo 1



Description

Designated path for air sampling purposes.

Photo 2



Description

Designated path for air sampling purposes.

Photo 3



Description

Designated path for air sampling purposes.

Photo 4



Description

Dust screens placement east of soccer field.

Photo 5



Description

Dust screens placement east of soccer field.

Photo 6



Description

Work area preparation completed.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/22/2015

Photo 1



Description

Dust Buster outside the work area for nozzle replacement.


Photo 2



Description

Law enforcement on site due to theft of Enviroscience's equipment.

Photo 3



Description

Law enforcement on site due to theft of Enviroscience's equipment.

Photo 4



Description

Recharge basin work area view from the west side.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/23/2015

Photo 1



Description

Gramercy trucks arrive at job site.


Photo 2



Description

Truck at lining station.

Photo 3

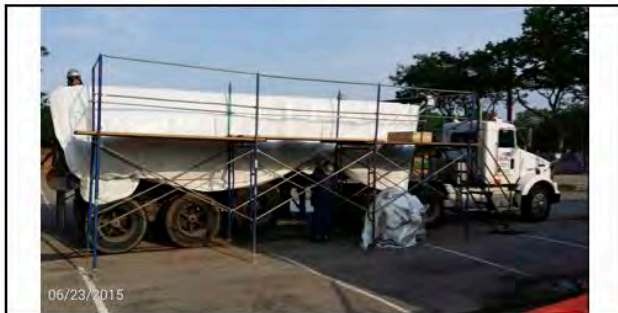

Description

Truck at lining station.


Photo 4



Description

Truck in loading area.

Photo 5

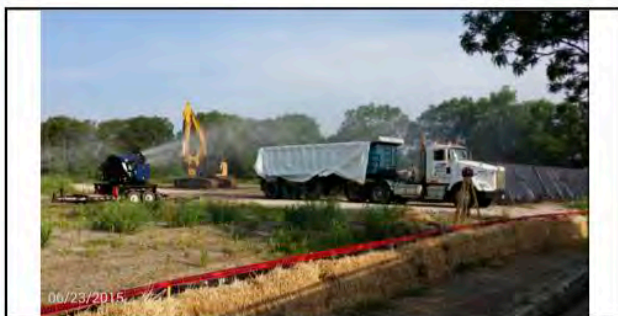

Description

Truck in loading area.

Photo 6



Description

Stock piling activities in progress.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/23/2015

Photo 1



Description

Stock piling activities in progress.

Photo 2



Description

Truck at covering station.

Photo 3



Description

Truck at covering station.


Photo 4



Description

Truck at tire wash station.

Photo 5

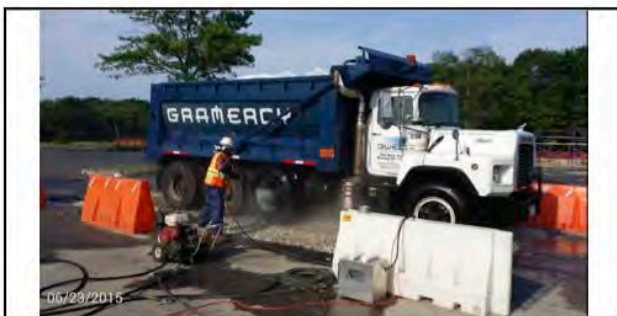

Description

Truck at tire wash station.

Photo 6



Description

Truck leaving the job site.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/23/2015

Photo 1



Description

Work area at end of shift.

Photo 2



Description

Work area at end of shift.

Photo 3



Description

Work area at end of shift.

Photo 4



Description

Work area at end of shift.

Photo 5



Description

Work area at end of shift.

Photo 6



Description

Work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/24/2015

Photo 1



Description

Trinity truck at lining station.

Photo 2



Description

Dust Screen placement.

Photo 3



Description

Dust Screen placement.

Photo 4



Description

Truck wetting parking lot work area.

Photo 5



Description

Wetted parking lot work area.

Photo 6



Description

Soccer field exposed material close up.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/24/2015

Photo 1



Description

Soccer field exposed material close up.

Photo 2



Description

Soccer field exposed material close up.

Photo 3



Description

Soccer field exposed material close up.

Photo 4



Description

Soccer field exposed material close up.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/24/2015

Photo 1



Description

Soccer field work area at end of shift.

Photo 2



Description

Soccer field work area at end of shift.

Photo 3



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/25/2015

Photo 1



Description

Dust Screen placement north of soccer field.

Photo 2



Description

Dust Screen placement north of soccer field.

Photo 3



Description

Equipment being serviced outside the work area.


Photo 4



Description

Equipment being serviced outside the work area.

Photo 5

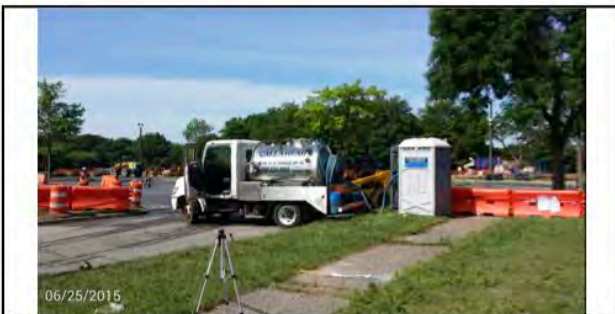

Description

Portable restrooms being serviced outside the work area.

Photo 6



Description

Gross removal activities in progress.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/25/2015

Photo 1



Description

Stock piling activities in progress.

Photo 2



Description

Stock piling activities in progress.

Photo 3



Description

Truck at lining station.

Photo 4



Description

Truck leaves the job site.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/26/2015

Photo 1



Description

Trucks lined up at beginning of the day.

Photo 2



Description

Gross removal activities in progress.

Photo 3



Description

Gross removal activities in progress.

Photo 4



Description

Gross removal activities in progress.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/26/2015

Photo 1



Description

Soccer field work area at end of shift.

Photo 2



Description

Soccer field work area at end of shift.

Photo 3



Description

Soccer field work area at end of shift.

Photo 4



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/29/2015

Photo 1



Description

Gross removal activities in progress.

Photo 2



Description

Gross removal activities in progress.

Photo 3



Description

Gross removal activities in progress.

Photo 4



Description

Storage container delivered at job site.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/30/2015


Photo 1



Description

Work area wetting activities in progress.

Photo 2

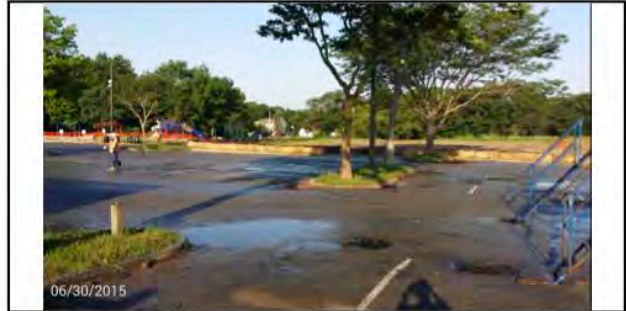

Description

Work area wetting activities in progress.

Photo 3



Description

Street sweeping activities in progress.


Photo 4



Description

Street sweeping activities in progress.

Photo 5

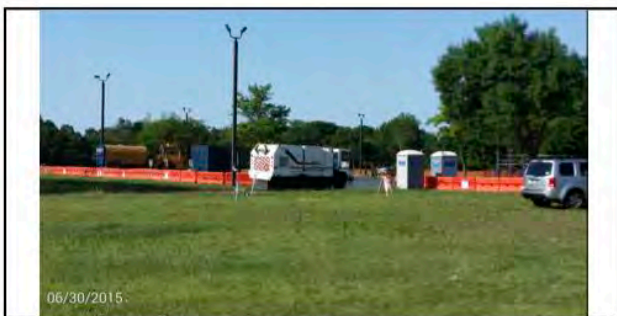

Description

Street sweeping activities in progress.

Photo 6



Description

Street sweeping activities in progress.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 6/30/2015

Photo 1



Description

Gross removal activities north of soccer field area in progress.

Photo 2



Description

Gross removal activities north of soccer field area in progress.

Photo 3



Description

Gross removal activities north of soccer field area in progress.

Photo 4



Description

Gross removal activities north of soccer field area in progress.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/1/2015

Photo 1



Description

Gross removal activities northwest of soccer field area in progress.

Photo 2



Description

Gross removal activities northwest of soccer field area in progress.

Photo 3



Description

Gross removal activities northwest of soccer field area in progress.

Photo 4



Description

Gross removal activities northwest of soccer field area in progress.

Photo 5



Description

Gross removal activities northwest of soccer field area in progress.

Photo 6



Description

Gross removal activities northwest of soccer field area in progress.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/1/2015

Photo 1



Description

Dust screen placement northwest side of soccer field.

Photo 2



Description

Dust screen placement northwest side of soccer field.

Photo 3



Description

Soccer field work area at end of shift.

Photo 4



Description

Soccer field work area at end of shift.

Photo 5



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/2/2015

Photo 1



Description

Gross removal activities northwest of soccer field area in progress.

Photo 2



Description

Gross removal activities northwest of soccer field area in progress.

Photo 3



Description

Gross removal activities northwest of soccer field area in progress.

Photo 4



Description

Soccer field south side wetting activities.

Photo 5



Description

Soccer field south side wetting activities.

Photo 6



Description

Soccer field south side wetting activities.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/2/2015

Photo 1



Description

Dust screen placement north side of soccer field.

Photo 2



Description

Dust screen placement north side of soccer field.

Photo 3



Description

Soccer field north side work area at end of shift.

Photo 4



Description

Soccer field north side work area at end of shift.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/6/2015

Photo 1



Description

Gross removal activities on soccer field area in progress.

Photo 2



Description

Gross removal activities on soccer field area in progress.


Photo 3



Description

Gross removal activities on soccer field area in progress.

Photo 4

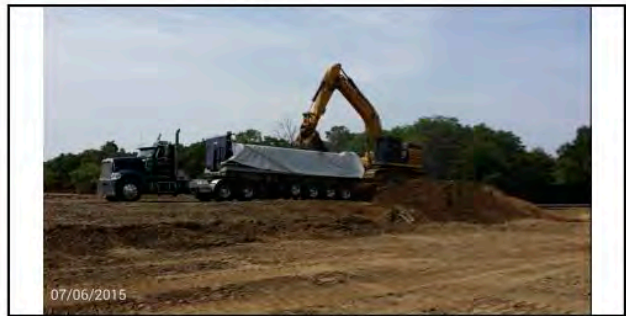

Description

Gross removal activities on soccer field area in progress.

Photo 5



Description

Gross removal activities on soccer field area in progress.

Photo 6



Description

Dust screen placement west side of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/6/2015

Photo 1



Description

Dust screen placement east side of soccer field.

Photo 2



Description

Wetting activities on south side of soccer field.

Photo 3



Description

Wetting activities on south side of soccer field.

Photo 4



Description

Soccer field work area at end of shift.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/7/2015

Photo 1



Description

CAT 320E excavator delivered at job site.

Photo 2



Description

Dust screen placement north side of soccer field.

Photo 3



Description

Gross removal activities on soccer field area in progress.

Photo 4



Description

Gross removal activities on soccer field area in progress.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/8/2015

Photo 1



Description

Gravel material delivered at job site.

Photo 2



Description

Dust screen placement north side of soccer field.

Photo 3



Description

Truck weighing trial run.

Photo 4



Description

Soccer field south side work area truck pathway.

Photo 5



Description

Gross removal activities on soccer field area in progress.

Photo 6



Description

Gross removal activities on soccer field area in progress.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/8/2015

Photo 1



Description

Gross removal activities on soccer field area in progress.

Photo 2



Description

Gross removal activities on soccer field area in progress.

Photo 3



Description

Wetting activities on parking lot area.

Photo 4



Description

Soccer field work area at end of shift.


Photo 5



Description

Soccer field work area at end of shift.

Photo 6

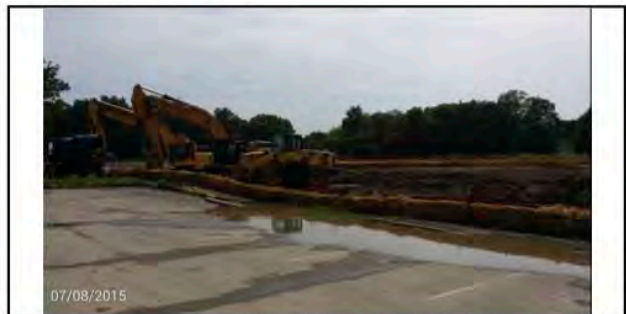

Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/9/2015

Photo 1



Description

Dust screen placement west side of soccer field.

Photo 2



Description

Gross removal activities on soccer field area in progress.

Photo 3



Description

Gross removal activities on soccer field area in progress.

Photo 4



Description

Soccer field work area at end of shift.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Trenching activities.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/9/2015

Photo 1



Description

Trenching activities.

Photo 2



Description

Trenching activities.

Photo 3



Description

Trenching activities.

Photo 4



Description

Trenching activities.

Photo 5



Description

Trenching activities.

Photo 6



Description

Trenching activities.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/9/2015

Photo 1



Description

Trenching activities.

Photo 2



Description

Trenching activities.

Photo 3



Description

Trenching activities.

Photo 4



Description

Soil sampling activities.

Photo 5



Description

Soil sampling activities.

Photo 6



Description

Soil sampling activities.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/10/2015

Photo 1



Description

Gross removal activities on soccer field area in progress.

Photo 2



Description

New work area boundary north of soccer field.

Photo 3



Description

Off island material stock piling activities in progress.

Photo 4



Description

Off island material stock piling activities in progress.

Photo 5



Description

Soccer field work area at end of shift north side.

Photo 6



Description

Soccer field work area at end of shift south side.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/13/2015

Photo 1



Description

Truck line up at beginning of shift.

Photo 2



Description

Truck line up inside the work area.

Photo 3



Description

Gross removal activities in progress north of soccer field.

Photo 4



Description

Gross removal activities in progress north of soccer field.


Photo 5



Description

Gross removal activities in progress south of soccer field.

Photo 6

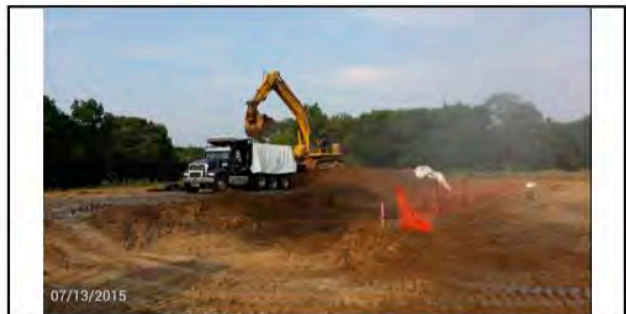

Description

Gross removal activities in progress south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/13/2015

Photo 1



Description

Truck weighing for off island material.

Photo 2



Description

CAT bulldozer delivered at job site.

Photo 3



Description

Work area at end of shift north of soccer field.

Photo 4



Description

Work area at end of shift north of soccer field.

Photo 5



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/14/2015

Photo 1



Description

Gross removal activities in progress north of soccer field.

Photo 2



Description

Gross removal activities in progress north of soccer field.

Photo 3



Description

Gross removal activities in progress south of soccer field.

Photo 4



Description

Work area at end of shift north of soccer field.

Photo 5



Description

Work area at end of shift north of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/15/2015

Photo 1



Description

Gross removal activities in progress north of soccer field.

Photo 2



Description

Gross removal activities in progress south of soccer field.

Photo 3



Description

Parking lot wetting activities in progress.

Photo 4



Description

Grading activities on north side of soccer field.

Photo 5



Description

Work area at end of shift north of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/16/2015

Photo 1



Description

Grading activities on north side of soccer field.

Photo 2



Description

Work area at end of shift north of soccer field.

Photo 3



Description

Work area at end of shift north of soccer field.

Photo 4



Description

Work area at end of shift north of soccer field.

Photo 5



Description

Work area at end of shift north of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.


Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/17/2015

Photo 1

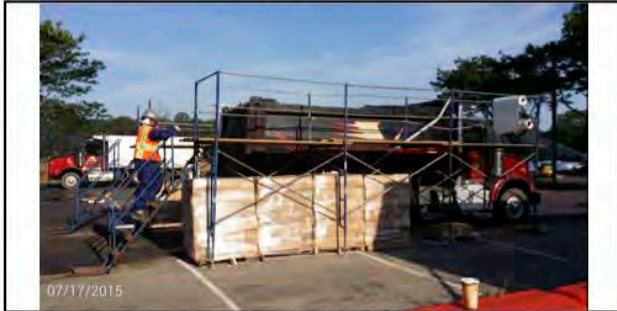

Description

Truck lining activities in progress.

Photo 2



Description

Dust suppression activities north of soccer field.

Photo 3



Description

Gross removal activities north of soccer field.

Photo 4



Description

Gross removal activities south of soccer field.

Photo 5



Description

Work area at end of shift north of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/20/2015

Photo 1



Description

Gross removal activities south of soccer field.

Photo 2



Description

Grading activities in progress north of soccer field.

Photo 3



Description

Grading activities in progress north of soccer field.

Photo 4



Description

Work area at end of shift north of soccer field.

Photo 5



Description

Work area at end of shift north of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/21/2015

Photo 1



Description

Gross removal activities south of soccer field.

Photo 2



Description

Gross removal activities south of soccer field.

Photo 3



Description

Gross removal activities south of soccer field.

Photo 4



Description

Gross removal activities south of soccer field.

Photo 5



Description

Gross removal activities north of soccer field at tree line.

Photo 6



Description

Grading activities in progress north of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/21/2015

Photo 1



Description

Grading activities in progress north of soccer field.

Photo 2



Description

Work area at end of shift north of soccer field.

Photo 3



Description

Work area at end of shift north of soccer field.

Photo 4



Description

Work area at end of shift north of soccer field.

Photo 5



Description

Work area at end of shift south of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/22/2015

Photo 1



Description

Gross removal activities north of soccer field.

Photo 2



Description

Gross removal activities south of soccer field.

Photo 3



Description

Gross removal activities south of soccer field.

Photo 4



Description

Work area at end of shift north of soccer field.

Photo 5



Description

Work area at end of shift north of soccer field

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/23/2015

Photo 1



Description

Gross removal activities north of soccer field.

Photo 2



Description

Gross removal activities south of soccer field.

Photo 3



Description

Stock piling activities south of soccer field.

Photo 4



Description

Stock piling activities south of soccer field.

Photo 5



Description

Work area at end of shift north of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/24/2015

Photo 1



Description

Truck lined up at beginning of shift.

Photo 2



Description

Gross removal activities north of soccer field.

Photo 3



Description

Gross removal activities south of soccer field.

Photo 4



Description

Stock piling activities south of soccer field.

Photo 5



Description

Work area at end of shift north of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/27/2015

Photo 1



Description

Gross removal activities south of soccer field.

Photo 2



Description

Stock piling activities south of soccer field.

Photo 3



Description

Soccer field work area at end of shift.

Photo 4



Description

Soccer field work area at end of shift.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/28/2015

Photo 1



Description

Gross removal activities south of soccer field.

Photo 2



Description

Stock piling activities south of soccer field.

Photo 3



Description

Soccer field work area at end of shift.

Photo 4



Description

Soccer field work area at end of shift.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/29/2015

Photo 1



Description

Truck line up at beginning of shift.

Photo 2



Description

Gross removal activities south of soccer field.

Photo 3



Description

Stock piling activities south of soccer field.

Photo 4



Description

Recharge basing area preparation.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Soccer field work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/30/2015

Photo 1



Description

Gross removal activities south of soccer field.

Photo 2



Description

Stock piling activities south of soccer field.

Photo 3



Description

Stock piling activities at recharge basin.

Photo 4



Description

Soccer field work area at end of shift.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Recharge basin work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 7/31/2015

Photo 1



Description

Gross removal activities on recharge basing.


Photo 2



Description

CAT excavator delivered at job site.

Photo 3

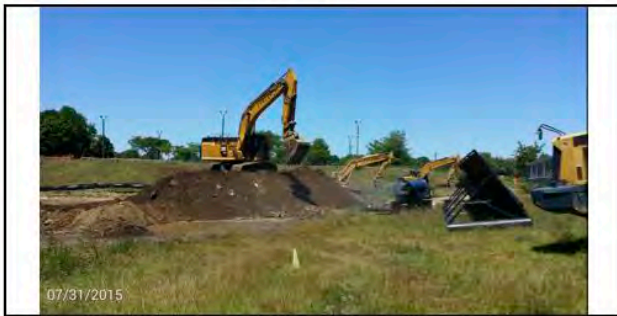

Description

Stock piling activities at recharge basin.

Photo 4



Description

Grading activities south of soccer field.

Photo 5



Description

Soccer field work area at end of shift.

Photo 6



Description

Recharge basin work area at end of shift.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/3/2015

Photo 1



Description

Gross removal activities south of soccer field.

Photo 2



Description

Gross removal activities south of soccer field.

Photo 3



Description

Stock piling and CAMP monitoring activities.

Photo 4



Description

Grading activities south of soccer field.

Photo 5



Description

Grading activities south of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/4/2015

Photo 1



Description

Gross removal activities south of soccer field.

Photo 2



Description

Stock piling activities south of soccer field.

Photo 3



Description

Grading activities south of soccer field.

Photo 4



Description

Work area at end of shift south of soccer field.

Photo 5



Description

Work area at end of shift south of soccer field.

Photo 6



Description

Work area at end of shift recharge basin.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/5/2015

Photo 1



Description

Gross removal activities south of soccer field.

Photo 2



Description

Gross removal activities at recharge basin.

Photo 3



Description

Work area at end of shift south of soccer field.

Photo 4



Description

Work area at end of shift south of soccer field.

Photo 5



Description

Work area at end of shift south of soccer field.

Photo 6



Description

Work area at end of shift recharge basin.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/6/2015

Photo 1



Description

Gross removal activities at recharge basin.

Photo 2



Description

Gross removal activities at recharge basin.

Photo 3



Description

Work area at end of shift north of soccer field.

Photo 4



Description

Work area at end of shift south of soccer field.

Photo 5



Description

Work area at end of shift recharge basin.

Photo 6



Description

Work area at end of shift recharge basin.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/7/2015

Photo 1



Description

Truck lining activities in progress.

Photo 2



Description

Gross removal activities at recharge basin.

Photo 3



Description

Gross removal activities at recharge basin.

Photo 4



Description

Gross removal activities at recharge basin.

Photo 5



Description

Excavator at wash station.

Photo 6



Description

Work area at end of shift recharge basin.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/10/2015

Photo 1



Description

Gross removal activities at recharge basin.

Photo 2



Description

Gross removal activities at recharge basin.

Photo 3



Description

Gross removal activities at recharge basin.

Photo 4



Description

Work area at end of shift recharge basin.

Photo 5



Description

Work area at end of shift recharge basin.

Photo 6



Description

Work area at end of shift recharge basin.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/11/2015

Photo 1



Description

Truck lining activities in progress.

Photo 2



Description

Gross removal activities at recharge basin.

Photo 3



Description

Stock piling activities at recharge basin.

Photo 4



Description

Stock piling activities at recharge basin.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/12/2015

Photo 1



Description

Gross removal activities at recharge basin.

Photo 2



Description

Stock piling activities in progress.

Photo 3



Description

Stock piling activities in progress.

Photo 4



Description

Work area at end of shift recharge basin.

Photo 5



Description

Work area at end of shift recharge basin.

Photo 6



Description

Work area at end of shift recharge basin.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/13/2015

Photo 1



Description

Gross removal activities at recharge basin.


Photo 2



Description

Gross removal activities at ramp to recharge basin.

Photo 3

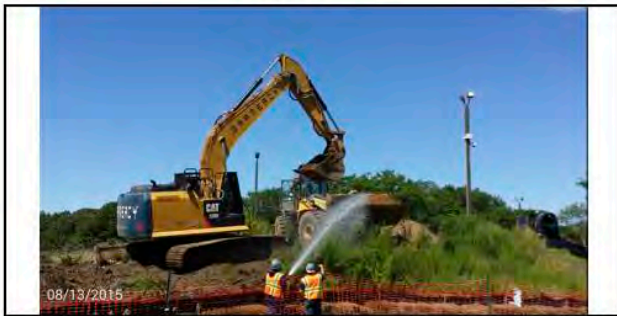

Description

Gross removal activities at ramp to recharge basin.

Photo 4



Description

Work area at end of shift recharge basin.

Photo 5



Description

Work area at end of shift ramp to recharge basin.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/14/2015

Photo 1



Description

Gross removal activities south of soccer field.

Photo 2



Description

Fine cleaning activities at ramp to recharge basin.

Photo 3



Description

Stock piling activities south of soccer field.

Photo 4



Description

Stock piling activities south of soccer field.

Photo 5



Description

Stock piling activities south of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/17/2015

Photo 1



Description

Equipment clean up activities in progress.

Photo 2



Description

Equipment outside the work area.

Photo 3



Description

Work area at end of shift north of parking lot.

Photo 4



Description

Work area at end of shift south of soccer field.

Photo 5



Description

Work area at end of shift south of parking lot.

Photo 6



Description

Work area at end of shift recharge basin.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/18/2015

Photo 1



Description

Gross removal activities in progress south of soccer field.

Photo 2



Description

Gross removal activities in progress south of soccer field.

Photo 3



Description

Gross removal activities in progress south of soccer field.

Photo 4



Description

Gross removal activities in progress south of soccer field.

Photo 5



Description

Work area at end of shift south of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.

Enviroscience Consultants
2150 Smithtown Avenue, Ronkonkoma, NY 11779

Daily Photo Log - Roberto Clemente Park, Soil Removal Project

Enviroscience Representative: Robert Cardona

Date: 8/19/2015

Photo 1



Description

Gross removal activities in progress south of soccer field.

Photo 2



Description

Gross removal activities in progress south of soccer field.

Photo 3



Description

Gross removal activities in progress south of soccer field.

Photo 4



Description

Work area at end of shift south of soccer field.

Photo 5



Description

Work area at end of shift south of soccer field.

Photo 6



Description

Work area at end of shift south of soccer field.
